# FACILITIES COUNCIL UPDATE

NOVEMBER 6, 2024



## WILLIAMSON WAY WATER INTRUSION REPAIR

- DISCOVERED WATER INTRUSION IN EARLY 2023
- COUNCIL AUTHORIZED \$139,000 IN TOTAL FUNDING
- COMPLETED PHASE 1 REPAIR OCTOBER 2023
- REMAINDER OF BUILDING REPAIRS COMPLETED IN SEPTEMBER 2024
- PROJECT SELF PERFORMED BY FACILITIES STAFF
- PROJECT FINISHED WITHIN BUDGET, EVEN WITH EXPANSION OF SCOPE


### WILLIAMSON WAY BEFORE








### WILLIAMSON WAY DURING

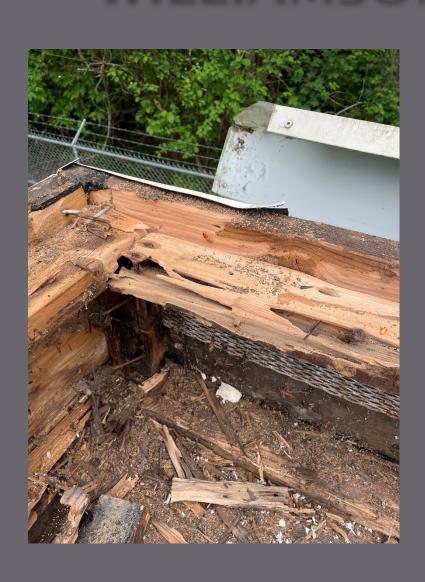

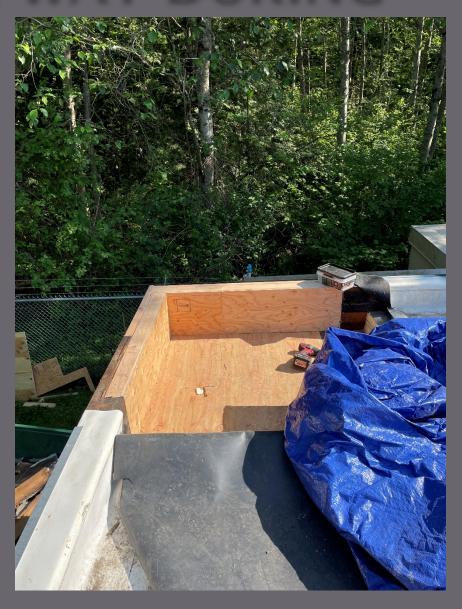

# WILLIAMSON WAY AFTER SUMMER 2023





### WILLIAMSON WAY SUMMER 2024



#### WAY STATION

- PROJECT BEGAN 2020 WITH PARTNERSHIP BETWEEN WHATCOM COUNTY, PEACE HEALTH, OPPORTUNITY COUNCIL AND UNITY CARE NORTHWEST
- FUNDING SOURCES (\$14.1MM)
- 1. COMMERCE GRANT (\$4MM)
- 2. FEDERAL GRANT (\$2MM)
- 3. AMERICAN RESCUE ACT (\$1.5MM)
- 4. HEALTH PERVISO GRANT (\$1.234MM)
- 5. FORMER STATE STREET PROJECT BASED BUDGET (\$2.4MM)
- 6. EDI (\$2.8MM)
- 7. BEHAVIOR HEALTH FUND (\$31K)

### WAY STATION BEFORE



# WAY STATION PROGRESS PHOTOS





### WAY STATION PROGRESS



### WAY STATION PROGRESS




#### WAY STATION

# OPENING OCTOBER 2024

# NORTHWEST ANNEX REDEVELOPMENT PROJECT

- COUNCIL AUTHORIZED \$5.1MM "SEED MONEY" FUNDING IN 2021
- STAFF BEEN WORKING WITH DESIGN TEAM TO DEVELOP SITE AND BUILDING DESIGNS
- OVERALL SITE CONSISTS OF 3 OFFICE BUILDINGS,
- INITIAL CONSTRUCTION PHASE ANTICIPATED TO INCLUDE BUILDING 1, AND THE SITE DEVELOPMENT OF THE ENTIRE SITE MAKING BUILDING 2 AND BUILDING 3 "PAD READY" PHASE 1 IS FRONT LOADED RELATIVE TO COSTS (MORE EXPENSIVE THAN NORMAL)
- AS PROJECT HAS DEVELOPED, BUILDING THE SHELL OF FUTURE BUILDING 2 (TO BE USED AS A STORAGE FACILITY) HAS EMERGED AS COST EFFECTIVE DEVELOPMENT
- CONSTRUCTING BUILDING 2 CONCURRENTLY WITH BUILDING 1 PROVIDES SUBSTANTIAL ECONOMIES OF SCALE AND VALUE

### NORTHWEST ANNEX DESIGN

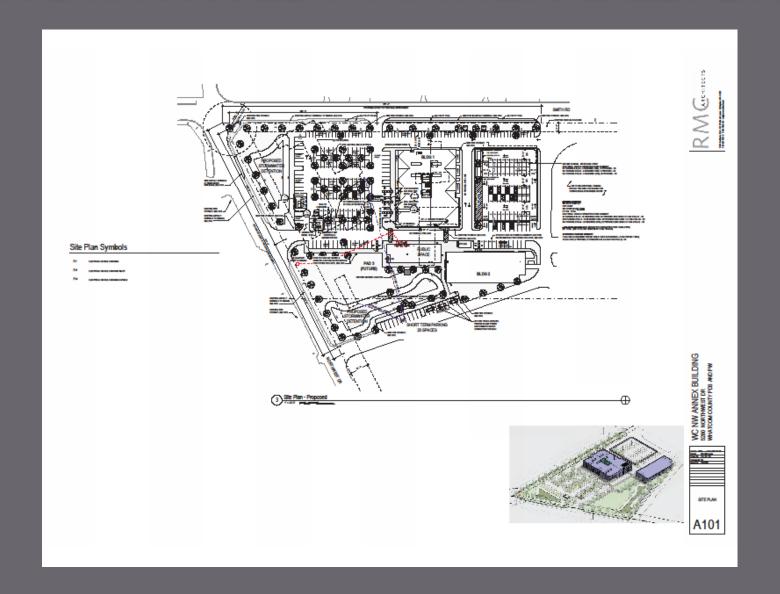

### NORTHWEST ANNEX DESIGN



### NORTHWEST ANNEX DESIGN



### NW ANNEX ESTIMATED COSTS

Phase 1 (Bidg 1) = \$26,287,380 Phase 2 (Bldg 2) = \$10,370,693

				7	\$26,287,380
				/	Phase 2 (Bldg 2) =
NW Annex Redvelopment Draw Schedule					\$10,370,693
Estimator	DCW		GLY		8 Ite = \$12,422,128
Building and Structures	Ś	59,004,960.00	\$ 48	,060,100.00	Total = \$48,060,100
Owners Contingency Add (same as design and constuction estimate)	\$	8,119,307.00		,914,835.00	
FF&E	Ś	1,579,867.00		.579.867.0	
Pro Rata Roundabout Share	Ś	500,000.00		500,000.00	
Building and Structures Total	\$	69,204,134.00	\$ 55,	,054,802.00	
A&E Costs					
RMC Contract	\$	1,782,484.00	\$ 1	,782,484.00	
RMC CO#1	Ś		\$	-	
RMC CO#2	\$		\$	-	
RMC CO#3	\$	926,931.00	\$	926,931.00	
RMC CO#4	\$	216,640.50	\$	216,640.50	
Possible COPs for Additional Scope			\$	50,000.00	
A&E Total	\$	2,926,055.50	\$ 2,	,976,055.50	
Utilities Costs					
Well Decommissioning	Ś	50,000.00	Ś	50,000.00	
Utility Connection Fees - PSE	\$	35,000.00		35,000.00	
Utility Connection Fees - Astound	\$	30,000.00		30,000.0=	
Fire Line Extension	Ś	250,000.00	\$	250,000.00	
Central Shops Fiber Reroute	ŝ	50,000.00		50,000.00	
Drill New Well for Soccer Fields	\$	10,000.00	Ś	10,000.00	
DITE THE THE STATE OF THE STATE	7	10,000.00	~	20,000.00	
Utilitiy Connection Fees - City of Ferndale (sewer and water)	Ś	10,000.00	Ś	10,000.00	
Utilities Total	\$	435,000.00	\$	435,000.00	
Permit Fees					
Permits/ Plan Review Fees	Ś	100,000.00	Ś	65.000.00	
Transportation Fees	Ś	17,000.00		17,000.00	
Total Permit Fees	Ś	117,000.00	Ś	82,000.00	
		221,0001100	*		
Pre-Construction Costs					
Soccer Field Locates	\$	2,500.00	Ś	2,500.00	
NW Annex Locates	\$	2,500.00	-	2,500.00	
Survey	\$	50,000.00		50,000.00	
Hazardous Material Abatement	Ś	39,690.00		39,690.00	
Total Pre-Construction Costs	Ś	94,690.00	Ś	94,690.00	
		- 4	*		
County Additional Construction Costs				$\neg \neg$	
Commissioning (\$ 26,000 incl. GLY estimate D3010)	Ś		Ś		
LEED (Incl. Obrien 360) \$ for plaque misc. fees	Ś	2,500.00	Š	2.500.00	
Special Inspections	Ś	50,000.00		50.000.00	
Project Management	\$	200,000.00		200,000.00	
Facilities Staff	Ś	50,000.00		50,000.00	
Temporary Storage During Construction	Ś	15,000.00		15,000.00	
Staff Moving Expenses From Existing to Building 1	\$	94,500.00	Ś	94,500.00	
Security	\$	10,000.00	\$	10,000.00	
Hazardous Material CA Services	\$	12,000.00		12,000.00	
Archeaology Consultant	\$	24,000.00	\$	24,000.00	
Builders Risk Insurance (GC Provided?)	\$		\$		
County Additional Construction Costs Total	\$	458,000.00		458,000.00	
Total	\$	73,234,879.50		,100,547.50	
Sales Tax	\$	6,444,669.40		,200,848.18	
Grand Total w Tax	\$	79,679,548.90		301,395.68	
Existing Budget	\$	(5,100,000.00)	\$ (5,	,100,000.00)	

## JUSTICE PROJECT UPDATE WHAT ARE WE DOING?


- IN MAY, HIRED SPECIAL PROJECTS MANAGER TO LEAD EFFORT
- SINCE THEN, WORKING DILIGENTLY ON PUTTING SCOPE OF WORK TOGETHER FOR A OWNER'S REPRESENTATIVE WITH SUBSTANTIAL JAIL EXPERIENCE TO GUIDE THE COUNTY IN IT'S DECISION MAKING
- OWNER'S REPRESENTATIVE SOLICITATION SHOULD OCCUR IN NEXT MONTH
- DESIRE TO HAVE OWNERS REP. ON BOARD AND READY TO WORK JUST AFTER HOLIDAYS

## JUSTICE PROJECT UPDATE WHAT ELSE ARE WE DOING?

- EXAMINING DIFFERENT CONSTRUCTION DELIVERY METHODS- WHICH IS BEST FOR THE COUNTY
  - HARD BID (TYP.)- COUNTY AT RISK
  - GENERAL CONTRACTOR/ CONSTRUCTION MANAGER (GCCM)- SHARED RISK/STILL COUNTY RISK, BUT YOU DON'T GET TO SELECT YOUR SUB CONTRACTORS FOR TRADES (LOWEST BIDDER)
  - PROGRESSIVE DESIGN BUILD-DESIGN BUILDER TEAM INCLUDING CONTRACTOR/ARCHITECT AND OWNER- ALL SHARING RISK, CHOOSE SUB CONTRACTOR TRADES. ASSUMED BEST QUALITY PROJECT DELIVERY METHOD AND SCHEDULE ASSURANCE.

### JUSTICE PROJECT UPDATE 6 MONTH LOOK AHEAD: 1.OWNERS REPRESENTATIVE

- 2. PROGRAMMING- WHAT ARE WE ANTICIPATING THE FACILITY TO LOOK LIKE
- 3. MEET WITH CPARB FOR ALTERNATIVE DELIVERY METHOD APPROVAL
- 4. RFQ FOR DESIGN BUILDER

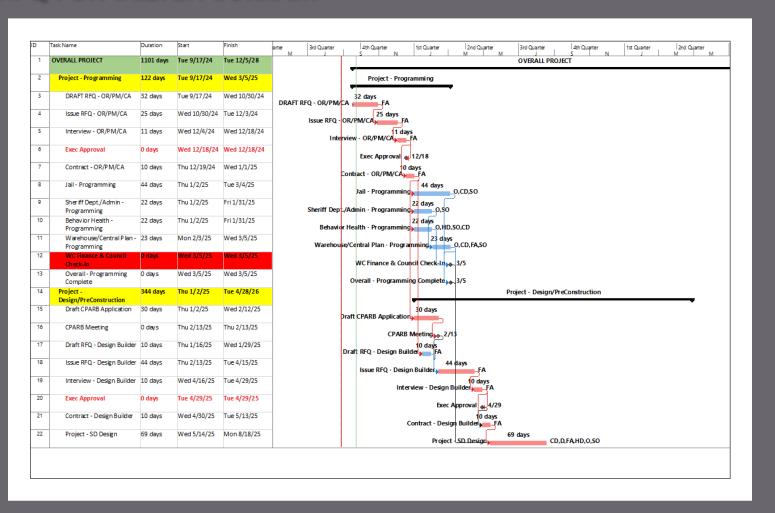

# JUSTICE PROJECT UPDATE THAT'S ALL GREAT- WHAT IS IT GOING TO COST?

Jail Project Costs (Sales Tax)			Sheriff's Office (REET)					
Site Construction & A/E @5.73% Costs	S	21,100,000.00	Sheriff's Admin/Dep	t Construction& A/E @5.73%	Costs		\$ 22,800,000.0	0
Jail Housing & Admin Construction & A/E@5.73%Costs	S	105,700,000.00	Warehouse (75%) (	\$ 5,000,000.0	0			
Warehouse (25%) Construction & A/E@5.73% Costs	\$	1,700,000.00	Morgue Constructio	n & A/E @5.73% Costs			\$ 4,300,000.0	0
Behavioral Health Center Construction & A/E@5.73% Costs	\$		Building Permitting				\$ 50,000.0	0
Behavioral Health Center - Grant	\$	(9,300,000.00)	Building Permitting -		\$ 30,000.0	0		
Existing Jail (Demo Only) Construction & A/E@5.73% Costs	\$		Testing Services		\$ 70,000.0			
Courthouse Holding Space	\$		Program Manageme				\$ 430,000.0	
Owner's Rep	\$		Third-Party Enhance	\$ 70,000.0 \$ 140,000.0				
Geotechnical Investigation	\$			FF & E Common Areas - Warehouse (Percentage)				
Traffic Analysis	\$	-1		FF & E Common Areas - Sheriffs				
Wetland Mitigation	\$		County Moving Cost		\$ 10,000.0			
Water and Sewer Connection Fees - Item 8&9 CUP	\$			- 5% of Construction			\$ 1,500,000.0	10
Storm Sewer Impact Fees - Item #12 CUP	\$	100,000.00	Combined Ferndale	Washington State Sales Tax	- 9.0% WSST		\$ 2,000,000.0	0
Building Permitting	S	300,000.00						
Building Permitting - Plan Check Fees	s	200,000.00					\$ 37,000,000.00	0
Planning Permitting - CUP Permit/SEPA	S	110,000.00						
Traffic Mitigation Fees - Per #7 CUP	S	500,000.00						_
Off-Site Development Costs	s	2,200,000.00		Jail SF Incl		Sheriff SF I		
Plant Investment & Tap Fees	\$	200,000.00		Site		Sheriff Admin/Dept	3200	
Testing Services	\$	500,000.00		Jail Housing/Admin		Warehouse(75%)	800	
Program Management Costs (Whatcom County Facilities, Corrections)	S	2,900,000.00		Warehouse (25%)		Morgue	500	00
Third-Party Enhanced Commissioning Fees @ \$1.50/SF	\$	500,000.00		Behavioral Health Center	15000			
FF & E Common Areas	\$	175,000.00		Ex. Jail	80000			_
FF & E Common Areas - Jail	\$	335,000.00		Satellite Office	5000			_
FF & E Common Areas - Warehouse (Percentage)	\$	50,000.00		SUB TOTAL SF	302400	SUB TOTAL SF	4500	
OFOI Building Technology and Communications Equip.	\$	550,000.00		% OF TOTAL SF	87.05%	% OF TOTAL SF	12.95	%
County Moving Costs	\$	60,000.00				GRAND TOTAL SF	34740	00
Building Art - 0.5% of Construction	\$	-						
Owner Contingency - 5% of Construction	s	7,000,000.00		Jail \$/BED @52	20 BEDS			
Combined Ferndale Washington State Sales Tax - 9.0% WSST	\$	9,400,000.00		\$	334,000.00			
	\$	173,939,000.00						
		, ,						
